Joint Base McGuire-Dix-Lakehurst
Restoration Advisory Board
22 October 2026

87th Air Base Wing





Welcome and Introductions
Review of hybrid RAB meeting format

Mr. James Richman

Remediation Program Manager, AFCEC/CZRE

•RAB –Restoration Advisory Board

"WIN AS ONE"

Announcements & Availability

- **Public Notices (PN)**
  - **Burlington County Times**
  - **Asbury Park Press**
  - **Pine Barrens Tribune**
  - **JB MDL RAB website: https://envirorestorejbmdl.com/**
    - **RAB presentation and minutes**
    - **PN**
    - **Limited CERCLA document requiring public notification**
- **Document Availability:**
  - **Burlington County Library (Westampton, NJ)**
  - **Ocean County Library (Toms River, NJ)**
  - **Air Force Administrative Record: https://ar.cce.af.mil/**

CERCLA – Comprehensive Environmental Response, Compensation, and Liability Act
JB MDL – Joint Base McGuire-Dix-Lakehurst
RAB – Restoration Advisory Board

"WIN AS ONE"

Community Engagement Events

- **Last Restoration Advisory Board (RAB): 26 March 2026**
  - **Public Comments were addressed at the meeting and included in the RAB minutes**
  - **Action Item:**
    - **BOMARC Mass Removal and Monitored Natural Attenuation**

PLANNED PRESENTATION TOPICS

- Action Items from 26 Mar 2026 Restoration Advisory Board Meeting
- Announcements
  - ESD - Lakehurst Area A/B
  - ESD - Lakehurst Area C
  - Lakehurst Five-Year Review (FYR)
- Remedial Actions
  - Lakehurst Site ZZ001 Remedial Action Field Results
  - Dix Site FR004 Remedial Action Field Results
  - Lakehurst ZZ003 Surface Sweep and CWM
  - McGuire Site LF019 Remedial Action
- Dix new Site TU972
- Contract Updates
  - Optimized Remediation Contract (ORC)
  - PFAS Background
  - RPMO MCL Contract
  - RPMO FYR

•CWM – Chemical Warfare Material
•ESD – Explanation of Significant Differences
•MCL – Maximum Contaminant Level
•PFAS – Per- and polyfluoroalkyl substances
•RPMO – Regional Program Management Office

"WIN AS ONE"





RAB Action Items
BOMARC Mass Removal and Monitored Natural Attenuation

Mr. Tom Crone

Project Manager, Arcadis, Inc.

•RAB – Restoration Advisory Board

BOMARC: OT016


- **Summary:**
  - **BOMARC is part of JB MDL-McGuire and located off SR-539 near Colliers Mills Wildlife Management Area**
  - **Two groundwater plumes (OT016 and WP005) are present and impacted by TCE, which was commonly used as a degreaser**
  - **A Record of Decision selecting Air Sparging and Monitored Natural Attenuation (MNA) to treat contaminated groundwater was signed in 2019 and installed in 2020.**
- **The RAB asked how much product/mass is being recovered in one month at the BOMARC site?**
  - **Product isn't actively recovered at BOMARC like it is at OU4 or TU003.**
  - **Contamination mass is being removed from groundwater through Air Sparge and Natural Attenuation; meaning it is not collected and difficult to calculate – but mass removal is evident in the declining groundwater concentrations.**
- **Tonight, we will share a comparison groundwater concentrations from 2020 and 2025.**

•JB MDL – Joint Base McGuire-Dix-Lakehurst •TCE - Trichoroethylene
•RAB – Restoration Advisory Board

BOMARC: OT016 Progress (concentration reduction)

OT016 Groundwater Plume in 2020

OT016 Groundwater Plume in 2025

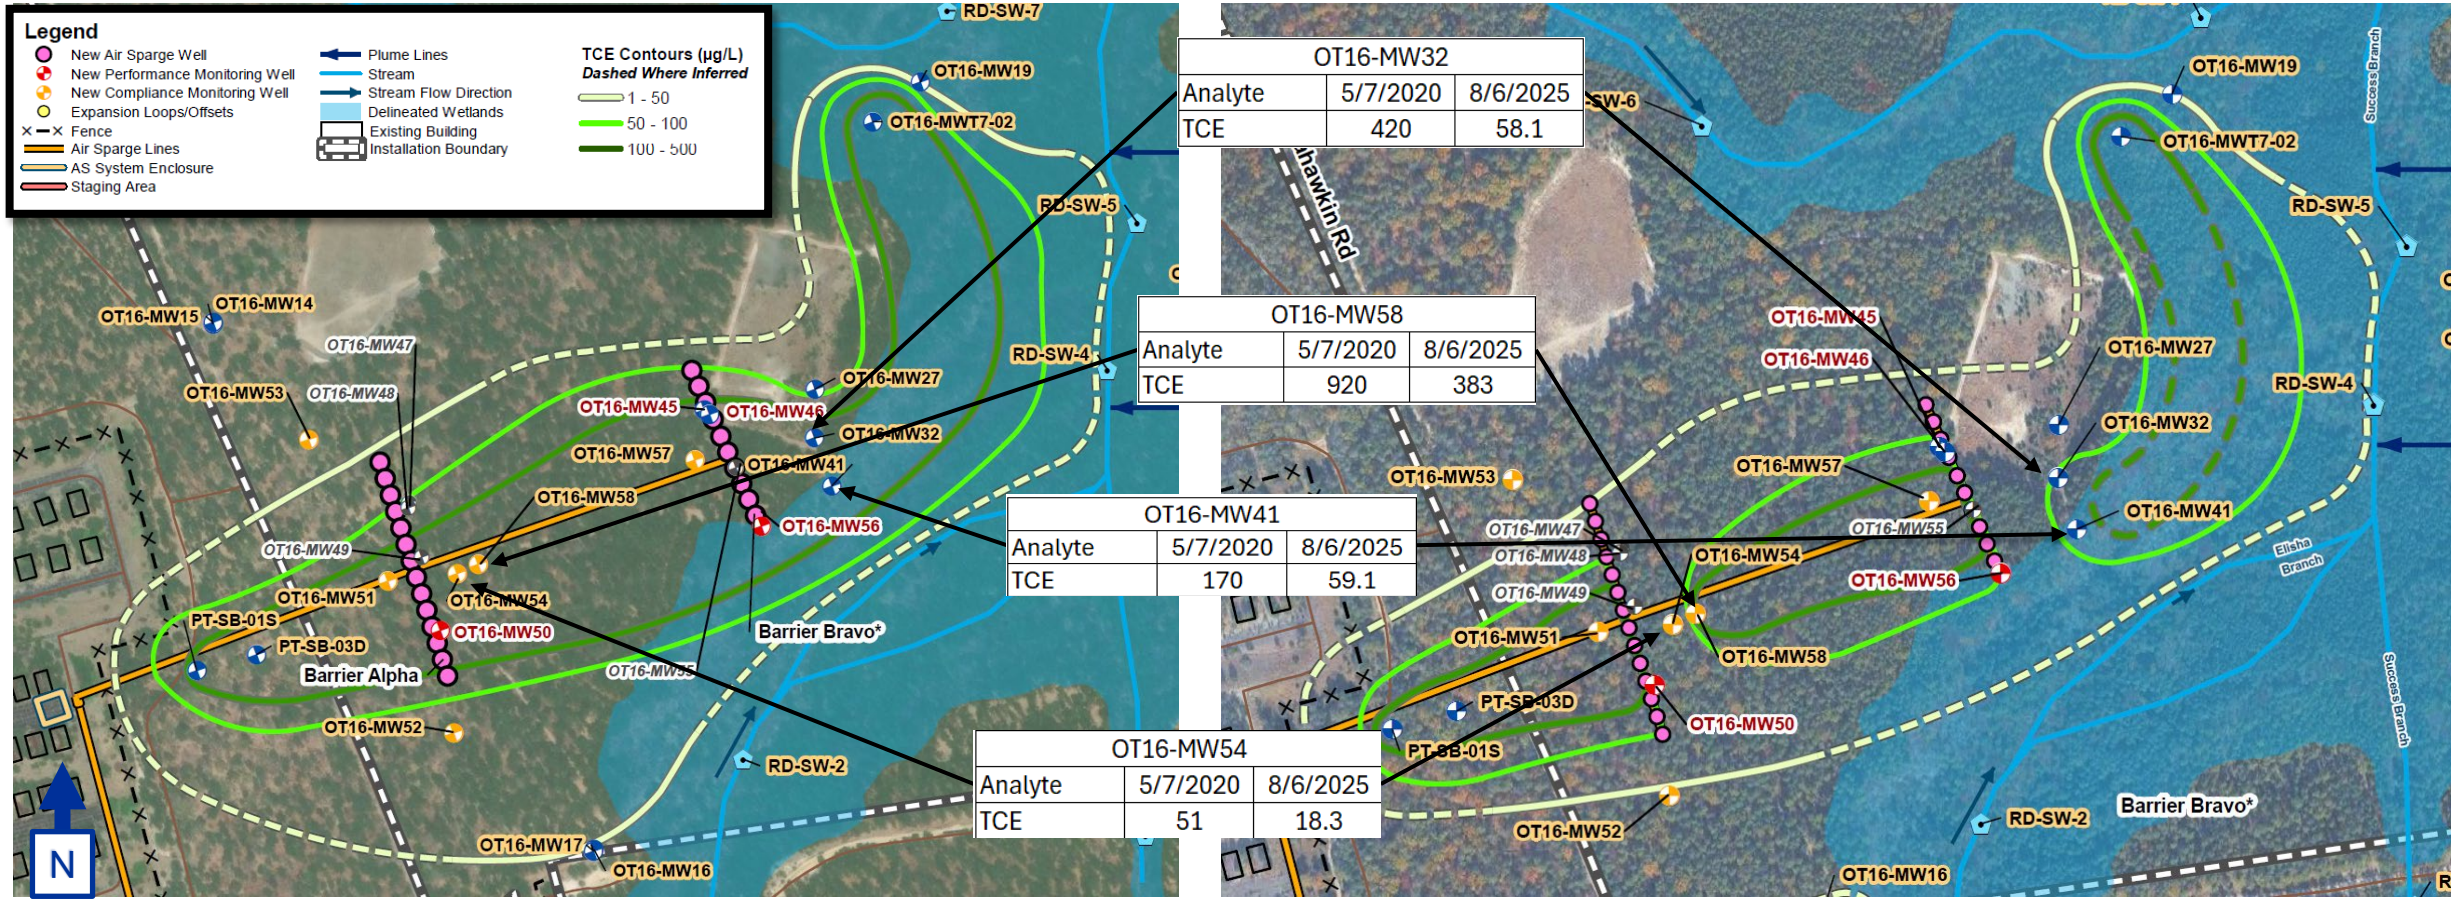


*Only databoxes for the baseline round of sampling and 2025 are shown. Cis-1,2-DCE and vinyl chloride are not shown. Additionally, data at only 4 wells is presented here.

DCE - Dichloroethylene
TCE - Trichloroethylene

"WIN AS ONE"

BOMARC: OT016 Progress (50 ug/L plume size reduction)

OT016 Groundwater Plume in 2020

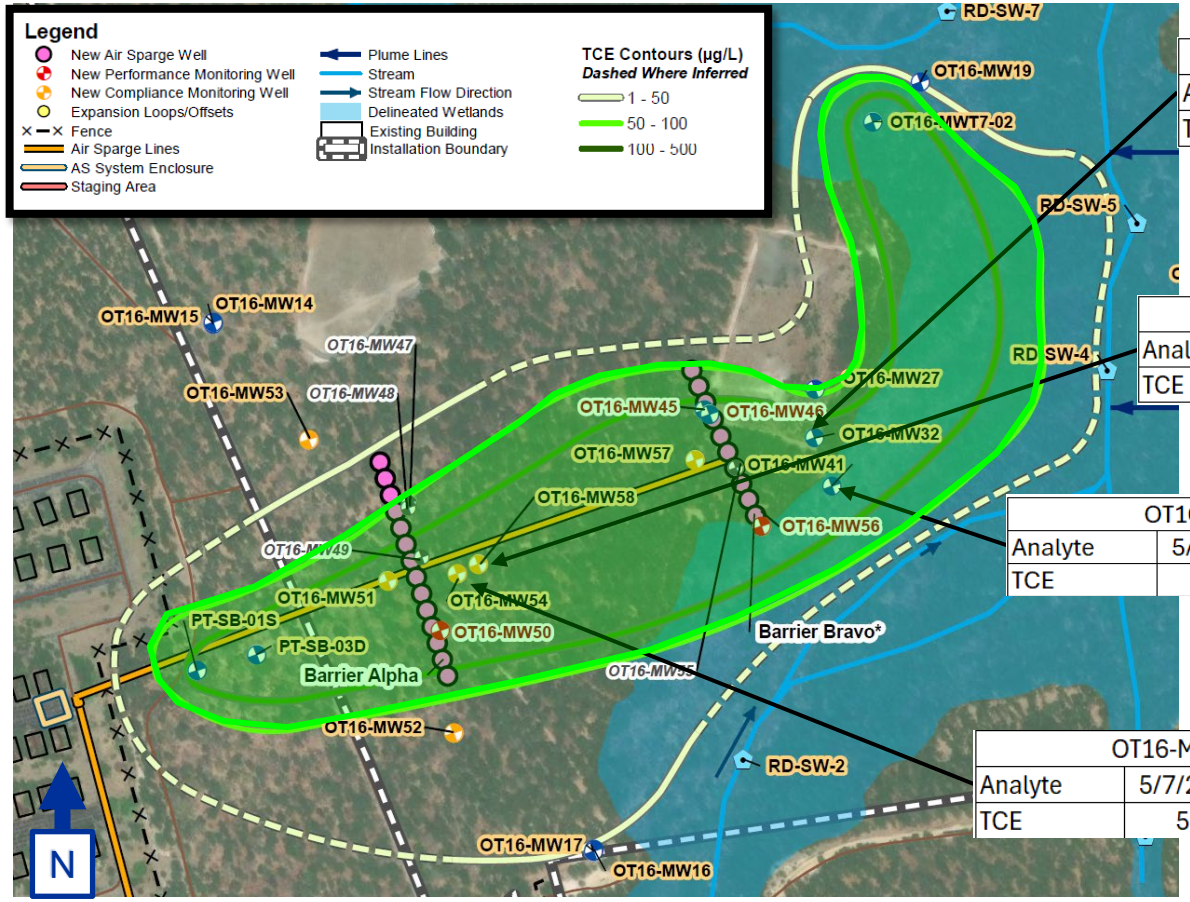


OT16-MW32		
Analyte	5/7/2020	8/6/2025
TCE	420	58.1

OT16-MW58		
Analyte	5/7/2020	8/6/2025
TCE	920	383

OT16-MW41		
Analyte	5/7/2020	8/6/2025
TCE	170	59.1

OT16-MW54		
Analyte	5/7/2020	8/6/2025
TCE	51	18.3

OT016 Groundwater Plume in 2025

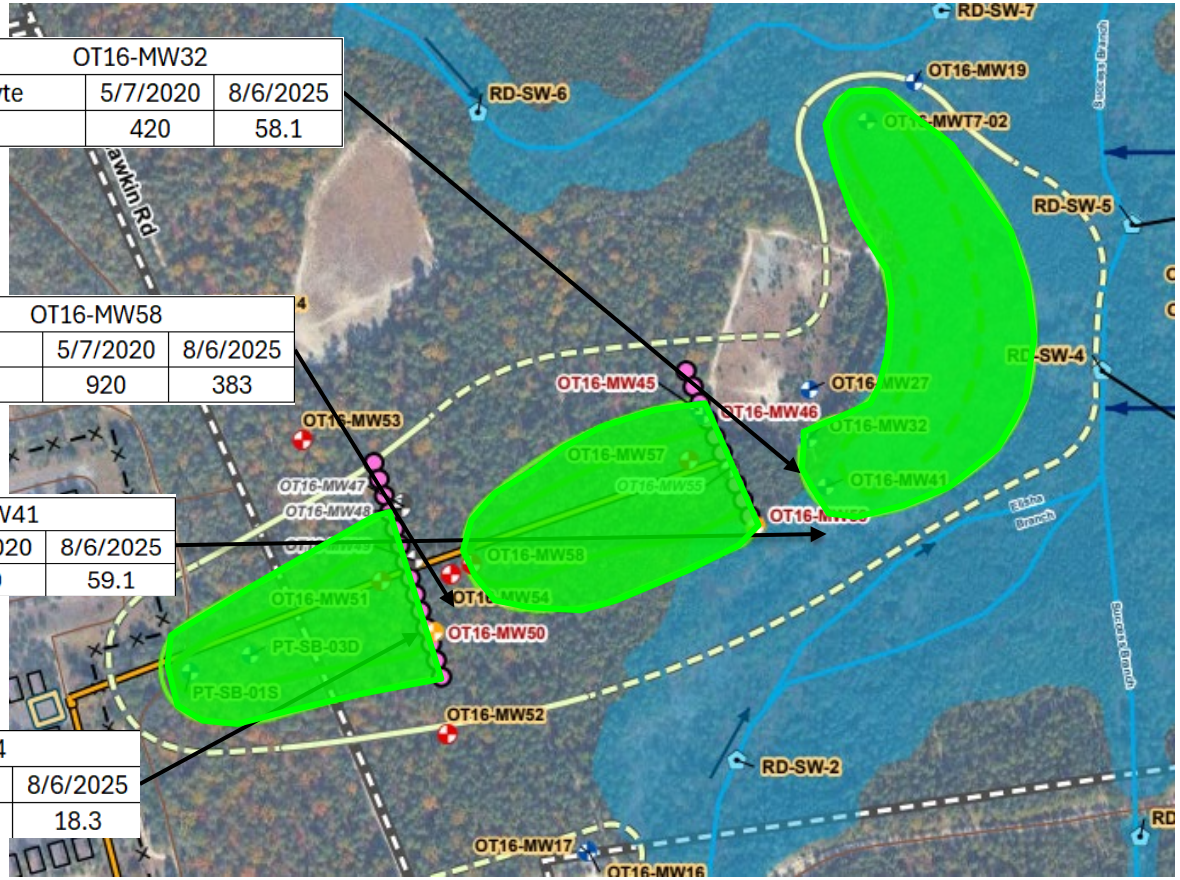

DCE - Dichloroethylene
TCE - Trichloroethylene

"WIN AS ONE"






Joint Base McGuire-Dix-Lakehurst
Explanation of Significant Differences
Area A/B and Area C

Ms. Samantha Saalfield

Deputy Project Manager, EA Engineering, Science, and Technology, Inc., PBC

Lakehurst Areas A/B ESD

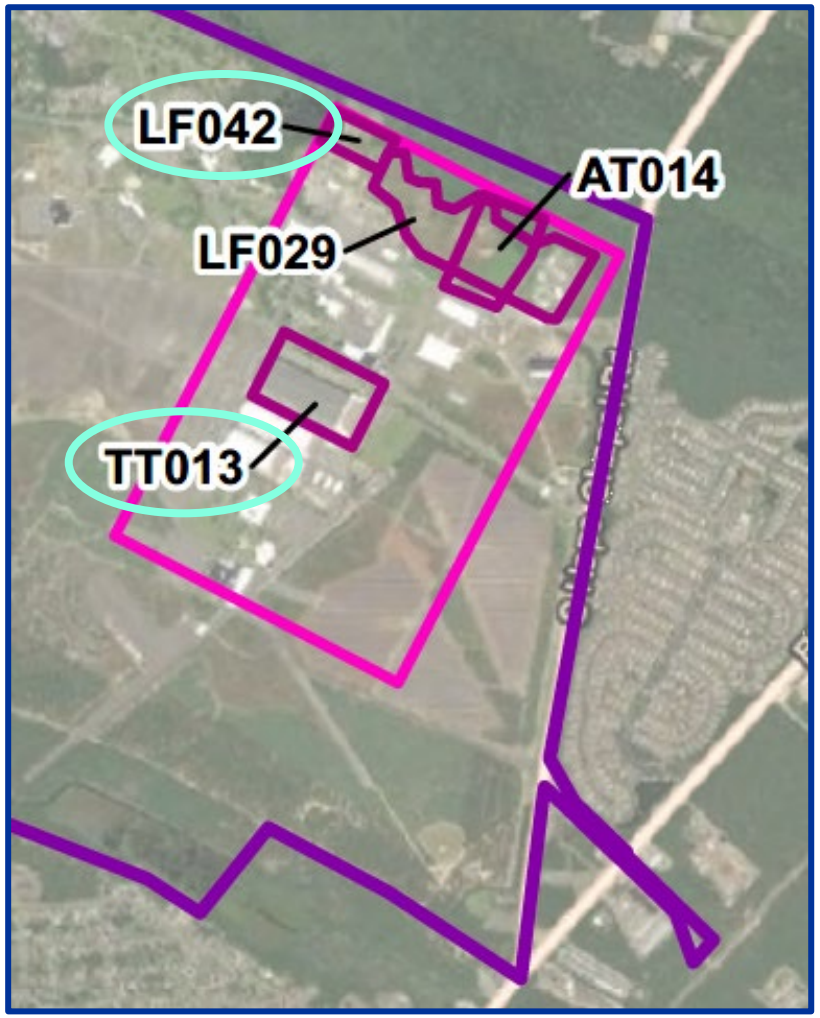


- ESD finalized July 2026.
- Documents changes in remedies by site, following decommissioning of groundwater pump and treat in 2024:
  - Air sparge/soil vapor extraction and activated carbon injections at Sites TT013 and LF042, where concentrations remain above remedial goals.
  - Monitored natural attenuation and attainment monitoring at Sites AT014 and LF029.

•ESD – Explanation of Significant Differences

"WIN AS ONE"

Lakehurst Area C ESD

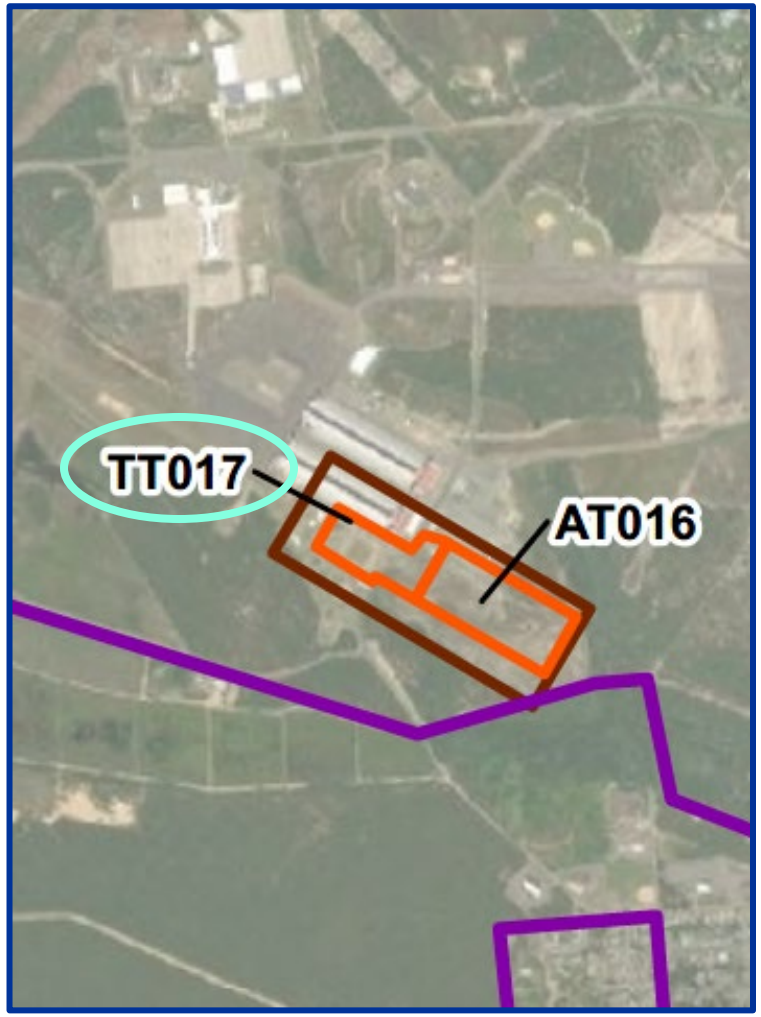

- ESD finalized July 2026.
- Documents changes in remedies by site, following decommissioning of groundwater pump and treat in 2024:
  - Air sparge/soil vapor extraction, biosparge, and activated carbon injections at Site TT017, where concentrations remain above remedial goals.
  - Biosparge and activated carbon injections at Site AT016.

•ESD – Explanation of Significant Differences





Joint Base McGuire-Dix-Lakehurst
Lakehurst Five-Year Review

Ms. Samantha Saalfield

Five-Year Review Lead, EA Engineering, Science, and Technology, Inc., PBC

On behalf of Hana-Bay West, LLC (Prime Contractor for Five-Year Review)

"WIN AS ONE"

Lakehurst Basewide Five-Year Review

Statutory Requirement for Five-Year Reviews

- Under CERCLA § 121(c), if a remedial action results in hazardous substances or contaminants remaining at the site above levels that permit unlimited use and unrestricted exposure, the remedial action must be reviewed every five years to assure that human health and the environment are being protected

- Fifth Lakehurst Five-Year Review – signed 9 September 2021.
- Sixth Lakehurst Five-Year Review – signed 12 August 2026.
  - Available at https://envirorestorejbmdl.com/community-involvement/

•CERCLA – Comprehensive Environmental Response, Compensation, and Liability Act

Lakehurst Basewide Five-Year Review

- The purpose of a five-year review is to determine whether the remedy implemented at a site is protective of human health and the environment
- Three core questions:
  A. Is the remedy functioning as intended?
  B. Are the assumptions used when the remedy was selected still valid?
  C. Has any other information come to light that could call into question the protectiveness of the remedy?
- <u>All</u> Lakehurst active CERCLA sites with remedies in place included in this review


•CERCLA – Comprehensive Environmental Response, Compensation, and Liability Act

"WIN AS ONE"

Lakehurst Basewide Five-Year Review, CERCLA Sites

SITE ID	Area	Site Name
SA004	K	Deadload Maintenance Shop
OW006	I/J	Catapult Test Facility
TT013	A/B	Former Fuel Farm No. 125
AT014	A/B	Old Fire Fighting School
AT016	C	NATTC Fire Fighting Training Area
TT017	C	Fuel Farm 196
LF029	A/B	Original Base Landfill
LF031	D	Former Sanitary Landfill
DP032	H	Launch End of the Test Tracks
LF042	A/B	Former Base Landfill

Lakehurst Five-Year Review Sites

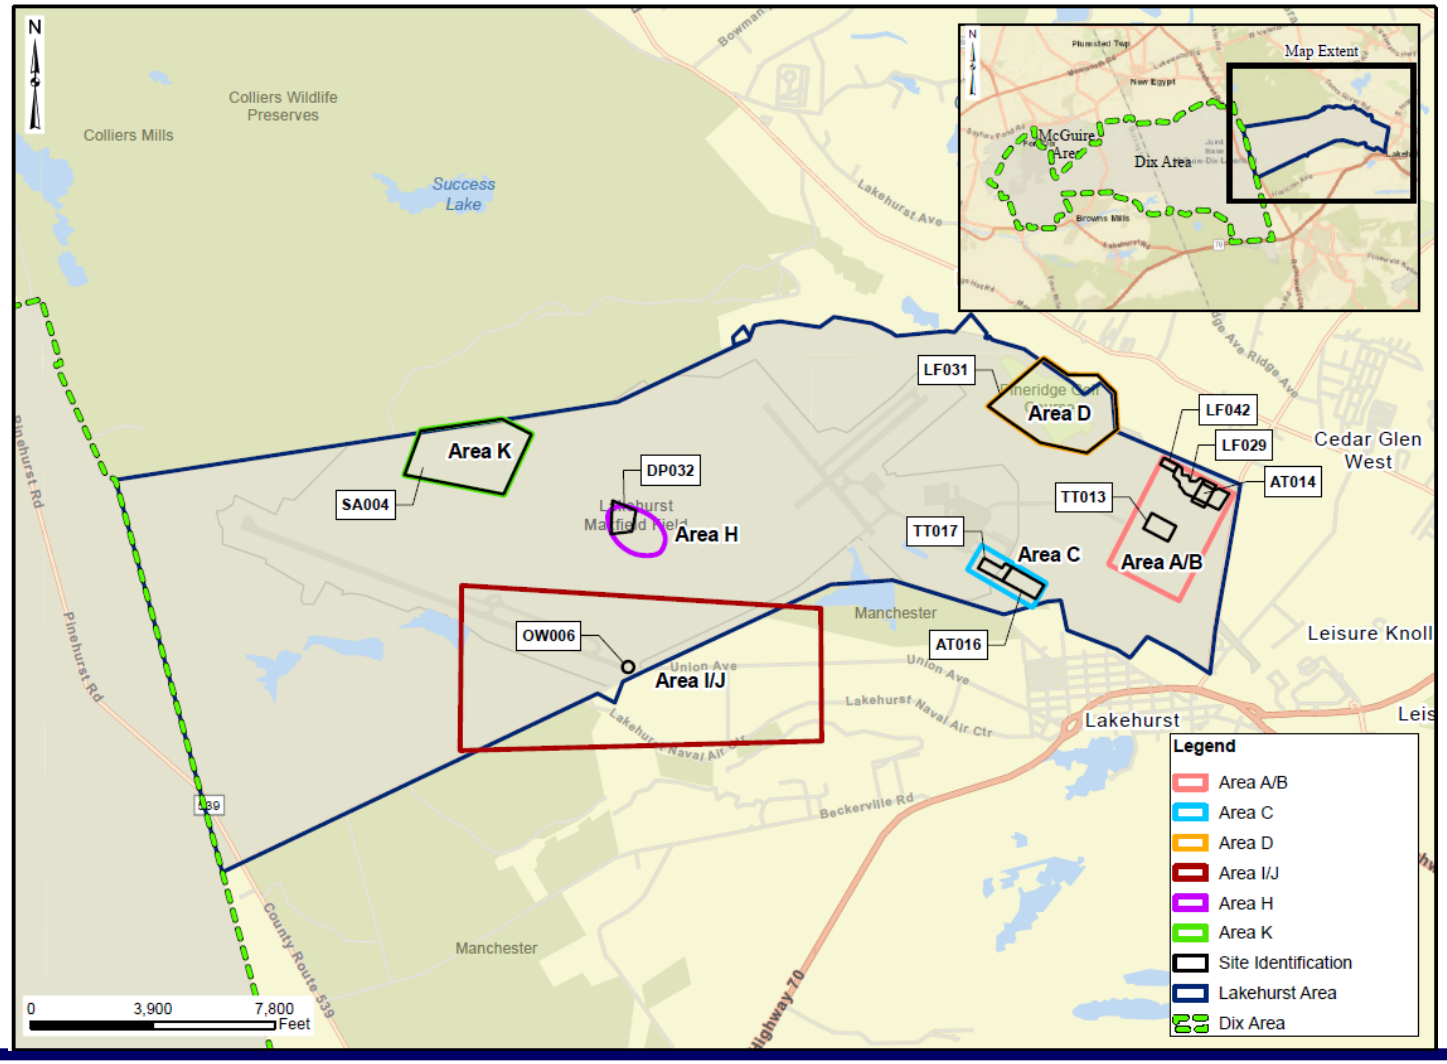

"WIN AS ONE"

Five-Year Review Report Contents

- Site history and background information
- Remedial action selection and implementation
- Observations of site inspection (conducted 16-17 March 2026)
- Summary of site interviews (conducted March 2026)
- Data review (January 2021 through June 2025)
- Technical assessment (address the 3 questions)
- Issues and Recommendations
- Protectiveness statement

Protectiveness Determination

- The remedies at all Areas are protective of human health and the environment with regard to the Records of Decision and associated COCs.
- Investigations are underway to delineate PFAS and 1,4-dioxane at JB MDL, and initial results indicate these emerging contaminants exceed screening criteria at one or more of the Lakehurst Five-Year Review sites. These investigations need to be completed to confirm long-term protectiveness.
- In the short term, known exposure pathways for PFAS in drinking water have been mitigated, and other potential exposure pathways for these contaminants that could result in unacceptable risks at these Areas are managed, monitored, and enforced through the implementation of land use controls, including the existing Groundwater Classification Exception Area.

COCs - contaminants of concern
JB MDL – Joint Base McGuire-Dix-Lakehurst
PFAS - per- and polyfluoroalkyl substances

Issues/Recommendations Potentially Affecting Long-Term Protectiveness

Areas A/B, C, D, H, and K:

- **Issue: PFAS have been detected at concentrations exceeding current screening levels.**
- **Recommendation: Complete the Remedial Investigation for PFAS and assess whether there are potential future unacceptable risks to potential receptors to determine whether a remedial action for PFAS is warranted to ensure protectiveness.**

Areas I/J:

- **Issue: 1,4-Dioxane has been detected at Site OW006 at concentrations exceeding the screening level (New Jersey practical quantitation level).**
- **Recommendation: Perform Step 2 evaluation of 1,4-dioxane at Site OW006.**

Other Actions/Recommendations

- **Areas A/B and C: Finalize explanations of significant differences to update the remedies to reflect remedy optimization and refine site specific groundwater contaminants of concern and remedial goals. *Finalized Summer 2026.***
- **Area H: Select a revised remedy to address remaining groundwater impacts and record the new remedy in a Record of Decision Amendment. *Planned for 2027.***
- **Areas D, I/J, and K: Continue future monitoring using contaminants of concern documented in the 2024 Technical Memoranda. *In progress.***
- **Areas D and K: Consider optimization measures, such as powdered activated carbon injections, to help accelerate the achievement of remedial goals for groundwater. *Coordinating with EPA and NJDEP.***
- **Area K: Consider the efficacy of spray aeration at Area K and whether it is advantageous to continue implementing this element of the remedy, given logistical limitations on its operation and the very low volatile organic contaminant concentrations remaining in groundwater. *Planned for 2027.***

"WIN AS ONE"

Lakehurst Basewide Five-Year Review

- The final, signed Five-Year Review Report is available at https://environrestorejbmdl.com/community-involvement/

- Public notices for finalization of the Five-Year Review were published 18-20 September in the Burlington County Times, Asbury Park Press, and Pine Barrens Tribune.

- The next Five-Year Review is planned to be submitted in September 2028. The USAF determined that a compressed review period is necessary to bring the five-year review schedule into agreement with the original trigger date of 27 September 1993, when the Record of Decision for Site TT013 was signed.





Former Lakehurst Submarine Bombing Target
Site ZZ001
Surface Clearance

Mr. Mike Figura


Remediation Program Manager, AFCEC/CZRE

MRS ZZ001 Layout and 1953 Historical Aerial Photo

- MRS ZZ001 is approximately 13 acres in size and is located in the southeastern portion of the Lakehurst Area of JBMDL.
- A target in the shape of a German U-boat was used by military aircraft at the site to drop practice or explosive bombs.
- The target was used from approximately 1933 to 1945.
- Official Navy documents from 1943 indicate that flights were conducted at 500 feet or less and that bomb drops were performed from about 50 feet above ground level almost daily in the early days of WWII.
- Pilots also released miniature bombs from airships for training purposes.



Surface Clearance Summary

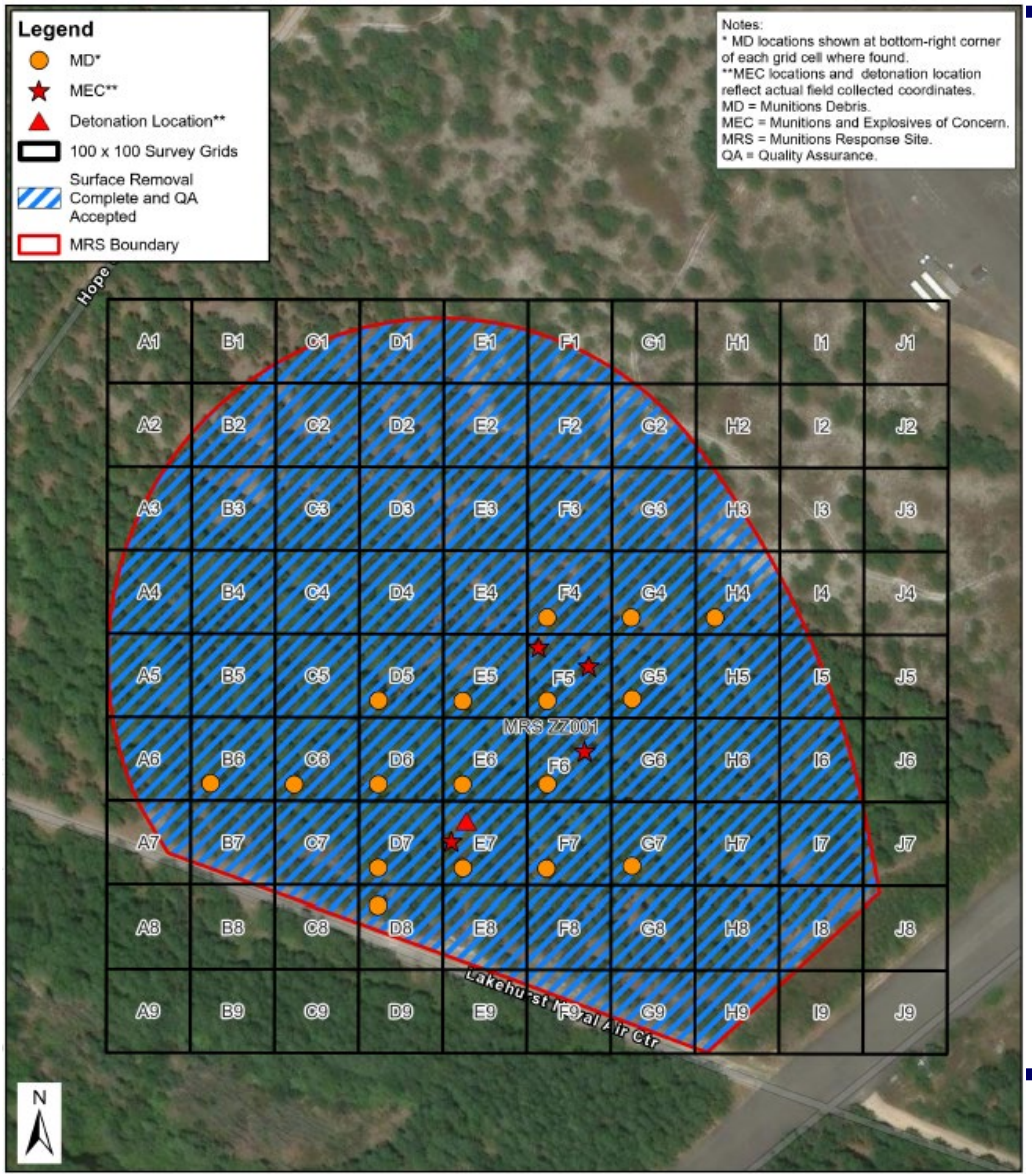



- 24 August to 11 September 2026
- Four MK23 three-inch practice bombs
- Detonated on 11 September 2026
- Munition debris found in 17 grids

"WIN AS ONE"

Summary





"WIN AS ONE"

ZZ001 Land Use Controls

- Land Use Controls (LUCs) include:
  - Limited vegetation removal
  - MEC Surface Clearance
    - Visual and instrument-guided MEC detection
    - Recurring surface MEC removal (every 5 years)
    - Proper destruction of MEC and subsequent off-base disposal of any resulting remnants or MD determined to be safe
  - Warning Signs
  - Dig Permit Process
  - Annual LUC Inspections
  - CERCLA Five-year Reviews



CERCLA – Comprehensive Environmental Response, Compensation, and Liability Act
MD – munitions debris
MEC – munitions and explosives of concern

"WIN AS ONE"






Former Dix Practice Mortar Range
Site FR004
Advance Geophysical Classification

Mr. Mike Figura

Remediation Program Manager, AFCEC/CZOE

Site Description

- Site FR004 (51 acres) is in the far western portion of the Joint Base McGuire-Dix-Lakehurst (JB MDL) Dix area
- Comprised of two distinctly separate areas (shown in orange):
  - a 46.88-acre irregularly shaped area located to the north, and
  - a 4.12-acre wooded area located south-southwest of the Grove Park housing area
- The northern portion of MRS FR004 is currently occupied by a portion of the Fountain Green golf course and recreational fields
- The southern portion of MRS FR004 (4.12 acres) is undeveloped, wooded land.

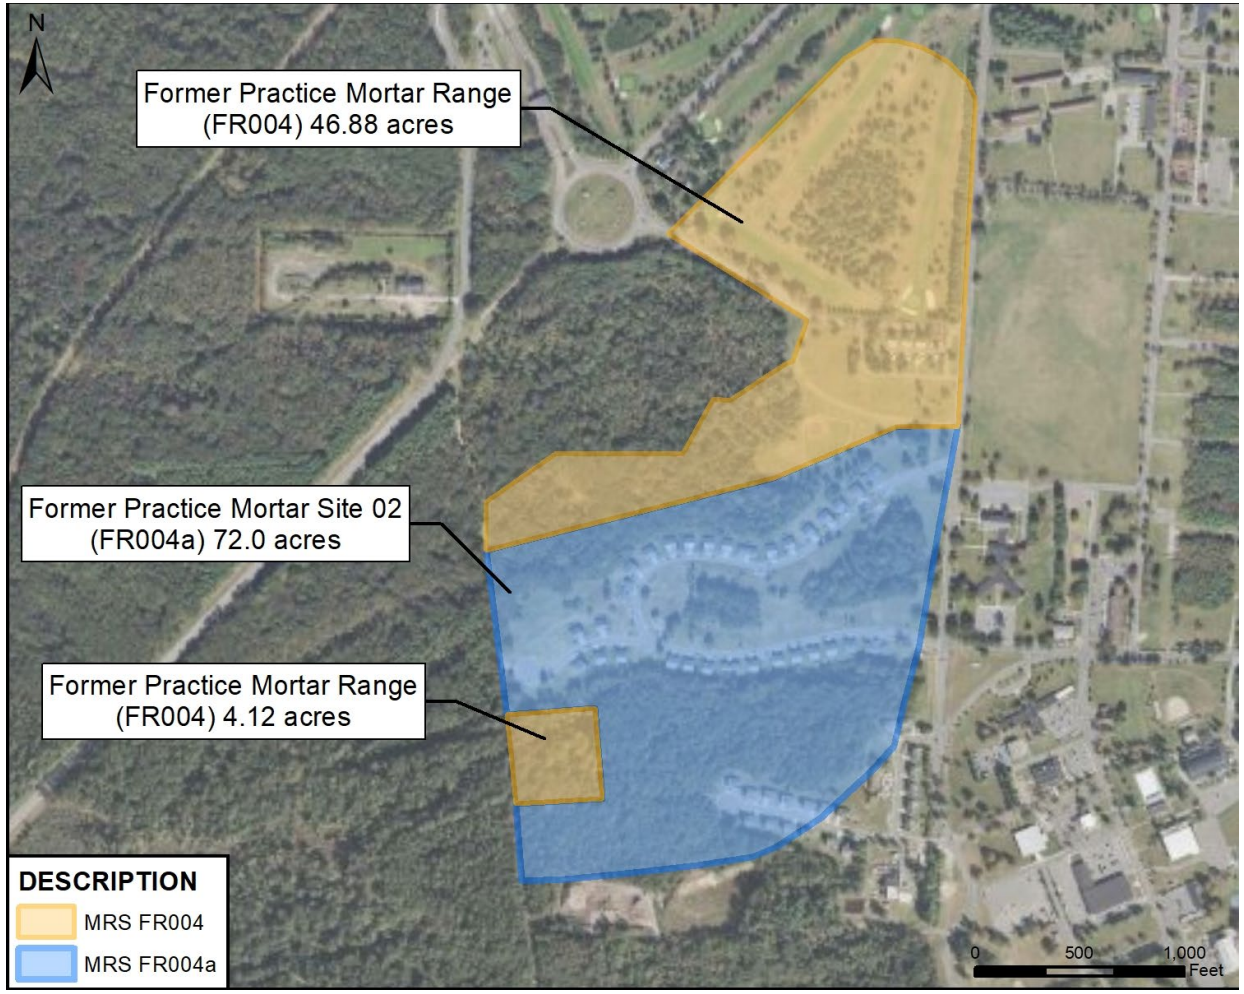

MRS – Munitions Response Site


"WIN AS ONE"

Selected Alternative for FR004: MEC Clearance

- **Munitions and Explosives of Concern (MEC) clearance and land use controls on the entire 4.12-acre southern portion of Munitions Response Site (MRS) FR004**
  - Vegetation clearance of all trees/brush 4 inches or less in diameter
  - MEC clearance to be conducted using Advanced Goephysical Classification (AGC)
  - If MEC is found, it would be excavated by hand
  - MEC disposal (if present) would be conducted by either consolidating the MEC that are acceptable to move for demolition or blow-in-place for MEC that are not acceptable to move
- **Land Use Controls (LUCs) would be established on the southern 4.12-acre area**
  - MEC clearance cannot prove to 100% certainty that no MEC will remain
  - Notification of the potential presence of MEC would be retained in the Base Master Plan and evaluated through the Dig Permit process
  - Five-Year Reviews
- **No action required in the 46.88-acre northern portion of the MRS**

Summary

- Area: 4.12 acres
- Quadrants: 100 ft x 100 ft (A1 through E5)
- Anomalies: 2645
- Saturated Areas: 6364 sqft (0.15 acres)
- Next Step: Advanced Geophysical Classification (AGC) cued data collection

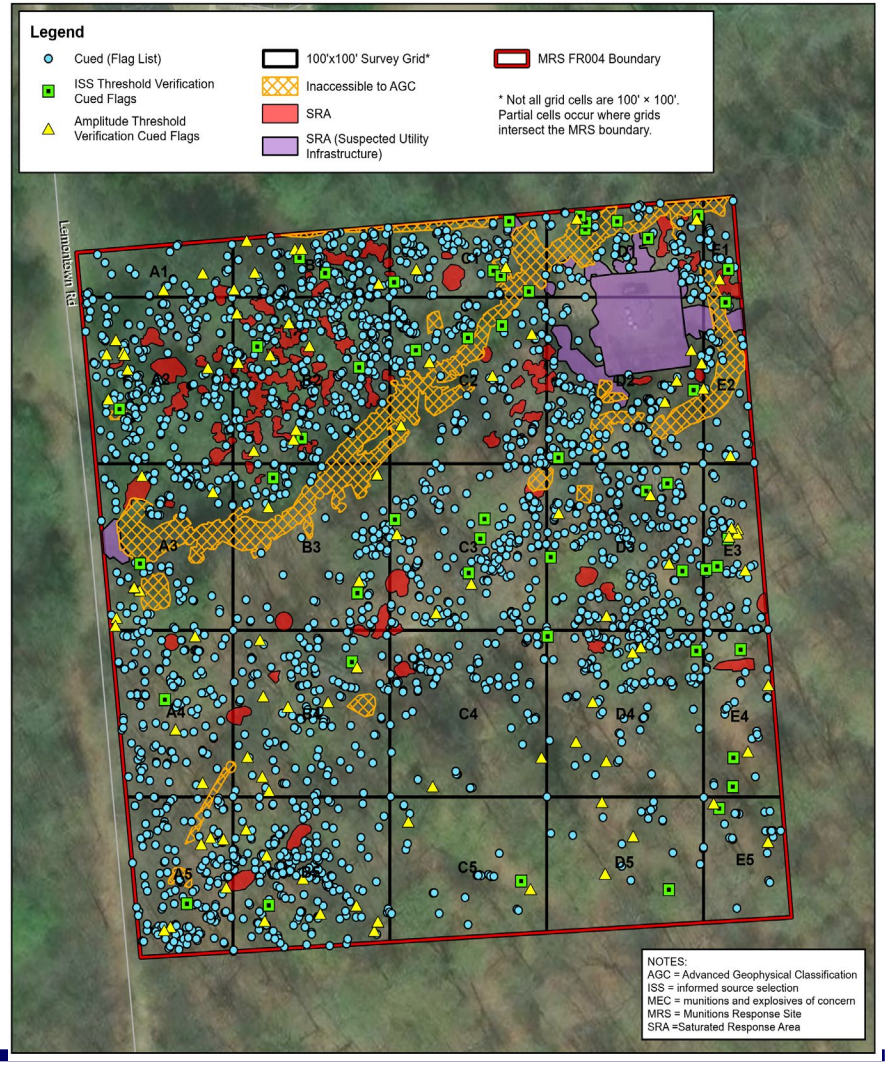

"WIN AS ONE"


Former Lakehurst Proving Grounds
Site ZZ003
Surface Clearance

Mr. Mike Figura

Remediation Program Manager, AFCEC/CZOE

Lakehurst Proving Grounds
Time Critical Removal Action (TCRA)

Objective: To identify and remove any munitions and explosives of concern (MEC) at or on the ground surface at the Lakehurst Test Track Area

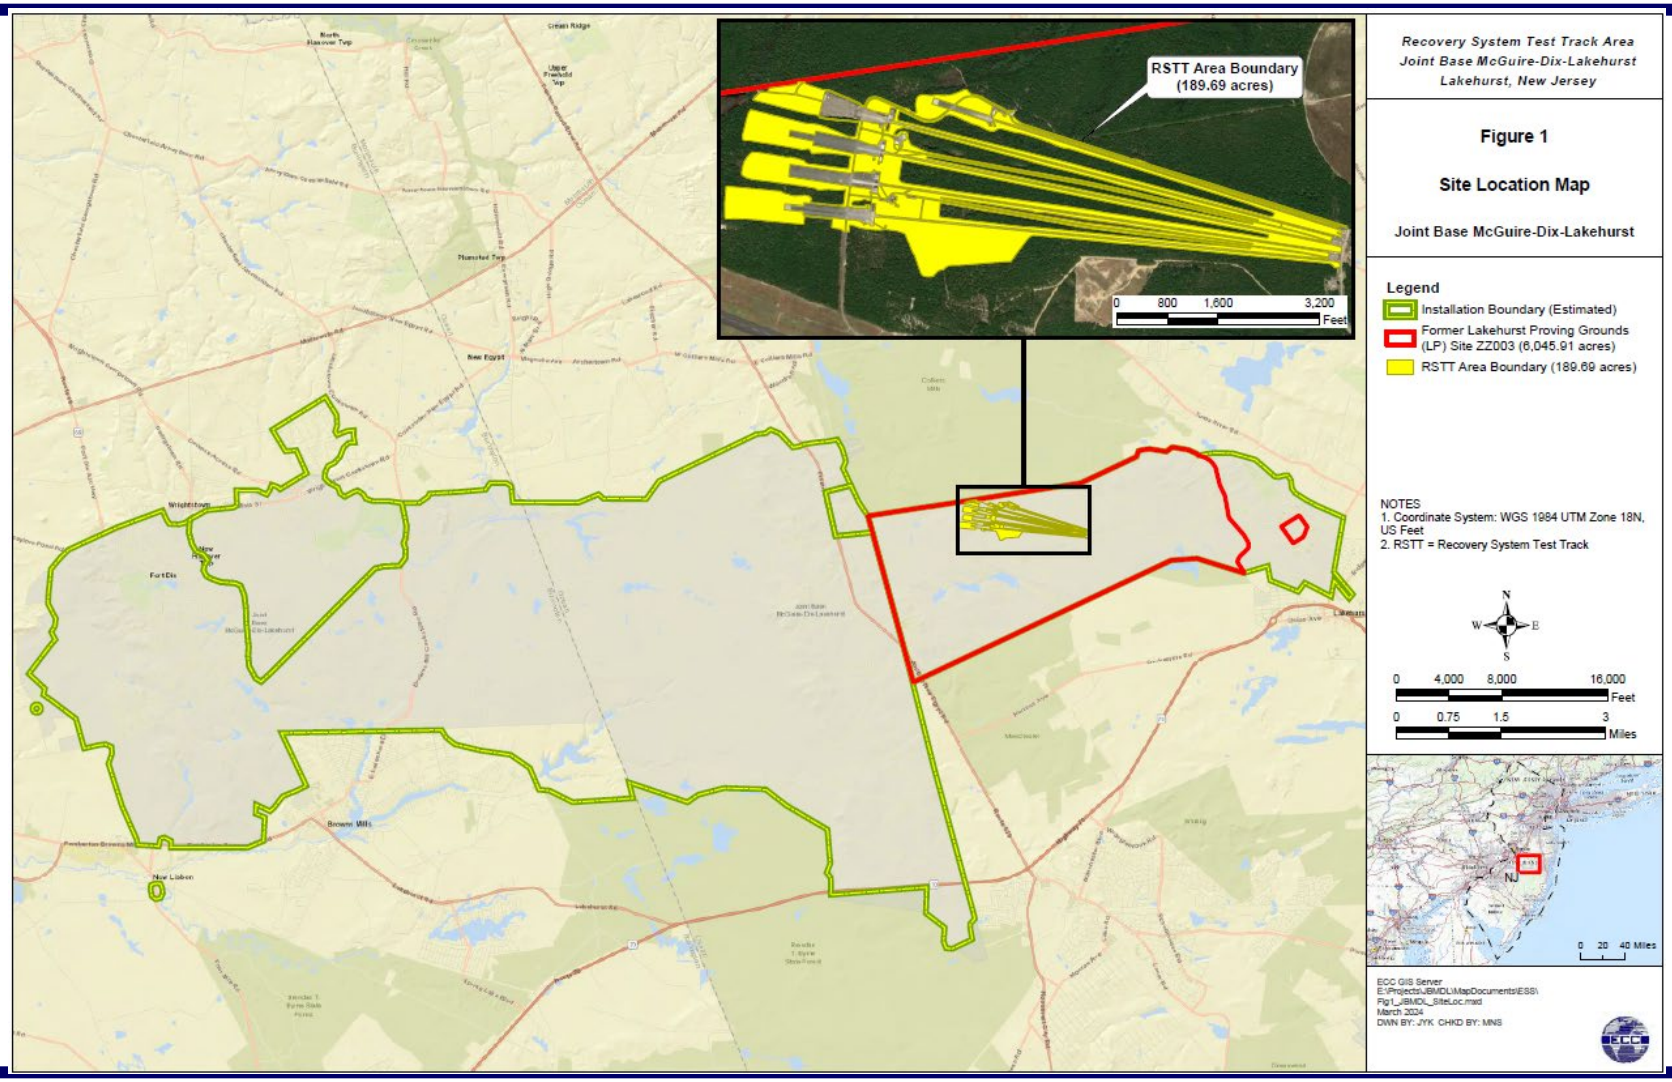

"WIN AS ONE"

Recovered 75 mm Projectile 3/24/2025



“WIN AS ONE”

Interim Holding Facility



"WIN AS ONE"

Lakehurst Proving Grounds
Surface Clearance Status as of 4/2/2025



"WIN AS ONE"

Status

Chemical Warfare Munition

- Maintain in Interim Holding Facility until destruction by Army

ZZ003 Surface Sweep

- Initial Effort Completed 2 April 2025
- 166 of 699 grids complete (36.7 acres of 186.8 acres, approx. 20%)
- Plan to Remobilize March 2027
- Updated Work Plan for Regulator Review
- Redo Vegetation Removal in early Spring 2027





Joint Base McGuire-Dix-Lakehurst
McGuire Site LF019 (Landfill 5) Remedial Action

Mr. Niels van Hoesel

Project Manager, FPM Remediations Inc.

Site LF019 History


- Part of Operable Unit-3 with LF002, LF020 and WP021
- Narrow, 5.5-acre parcel of land south of South Run
- Operated as a landfill from approximately 1970 to 1973
- Waste disposal primarily by burning bulk waste in-place, leveling the burned and unburned residue, and applying a clean soil cover
- Waste volume estimated at 82,000 cubic yards


Site LF019 History (continued)

- Non-Time Critical Removal Action: 2012
  - 2-ft soil cover, waste consolidation, and grading
  - Implemented within southeast portion of landfill
- OU3 Remedial Investigation: 2013
- OU3 Feasibility Study:2017
- OU3 Proposed Plan: 2017
- Time Critical Removal Action: 2021
  - 106-millimeter recoilless rifle cartridges discover in gulley. 3,408 items plus approximately 5,000 50-cal steel casings were removed in three separate mobilizations in 2021. The site was restored on both sides of the gulley and seeded.
- LF019 Record of Decision in 2024

•OU – Operable Unit

Site LF019 History

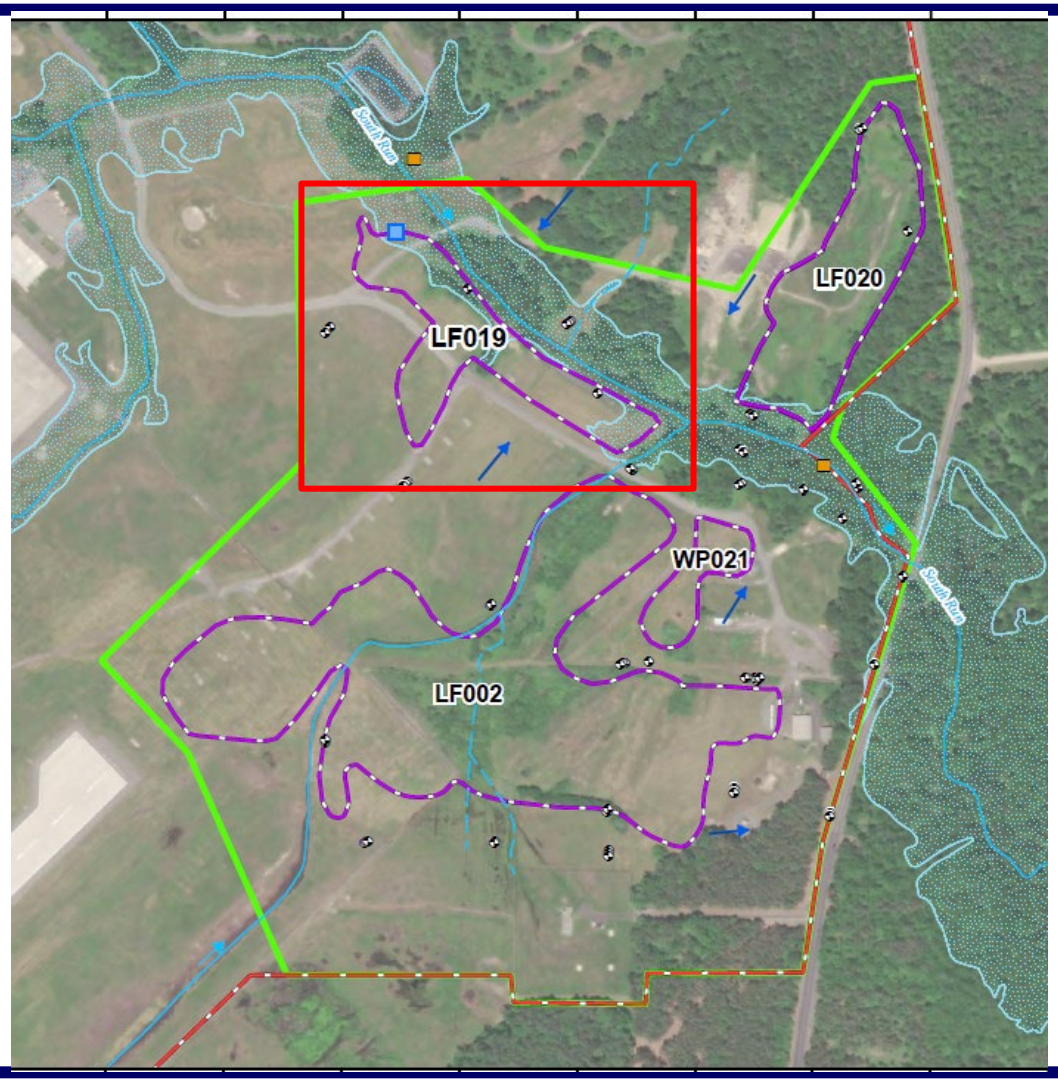

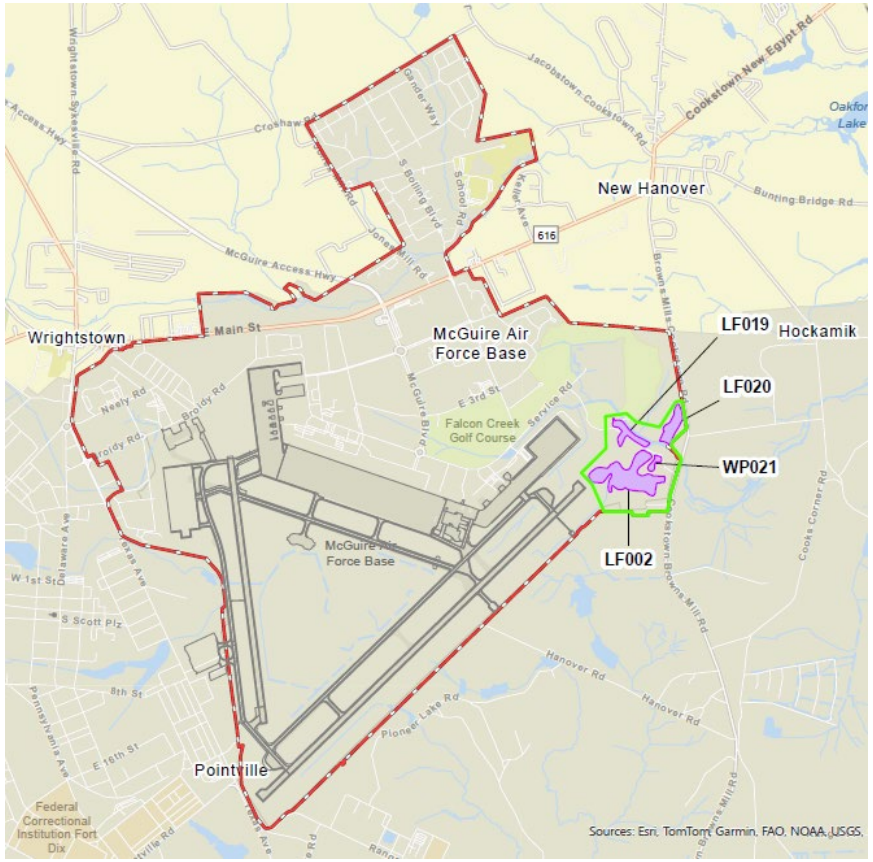

"WIN AS ONE"

Site LF019 Remedial Action


- LF019 Remedial Design. Originally part of OU3, but split off due to discovery of discarded military material in 2017
- Remedial Design components
  - 2-foot Soil Cover
    - The total soil cover area is approximately 3 acres and the calculated soil volume is 3,920 cubic yards (cy) (~261 trucks)
  - Groundwater and Surface Water Monitoring
  - Land Use Controls
- Approved by EPA and NJDEP in 2026

LF019		
Volume	**Unit**	**Number**
Subgrade volume	cy	716
Fill volume	cy	2,125
Topsoil volume	cy	1,080
Total volume	cy	3,920

•EPA – Environmental Protection Agency
•NJDEP – New Jersey Department of Environmental Protection
•OU – Operable Unit

"WIN AS ONE"

Site LF019 Remedial Action

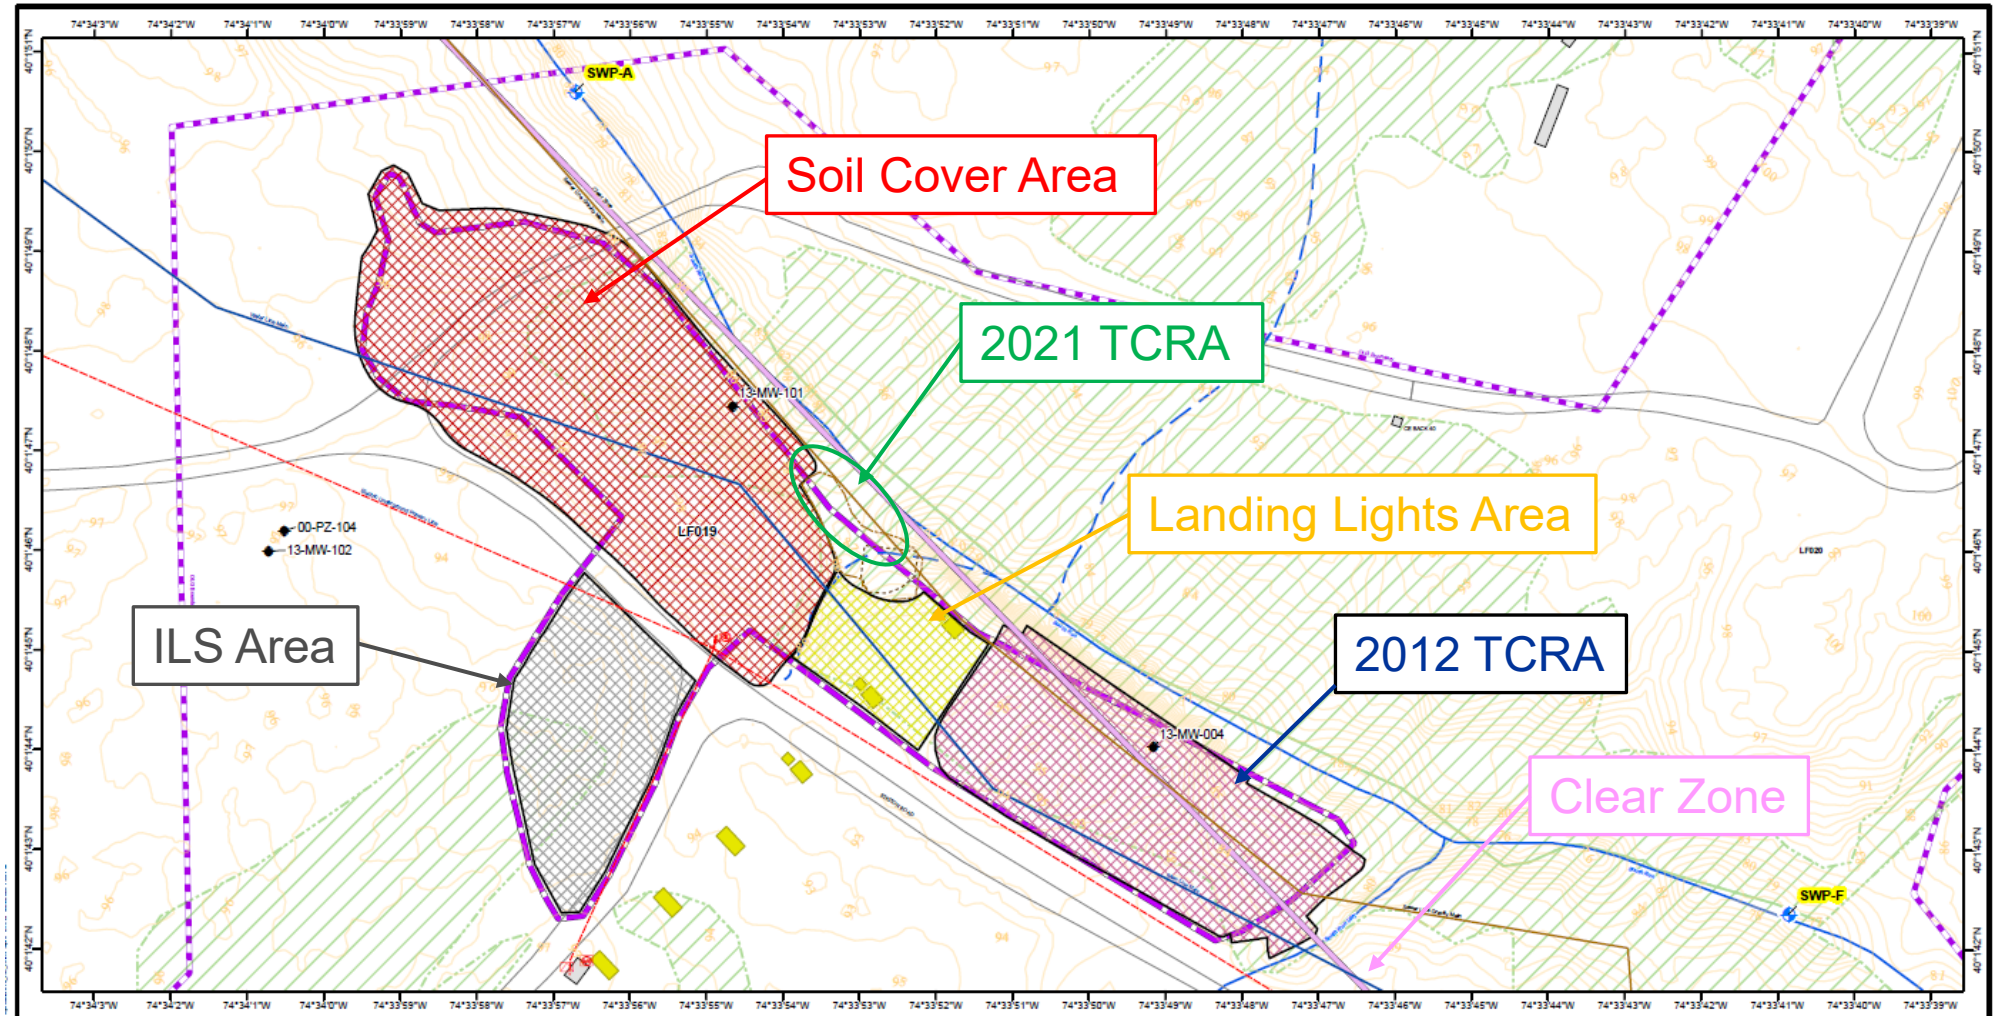

•ILS – Instrument Landing System
•TCRA – Time Critical Removal Action

"WIN AS ONE"

Site LF019 Remedial Action

- Scheduled for Winter/Spring 2026/2027 (after State ARARs document approval)
- Field work: 35 days
- Pre-construction tasks:
  - Deliberate risk assessment – pending USAF Operations approval
  - Kickoff meetings with USAF Operations and security
  - Utility mark out and dig permit
- Onsite work:
  - Ancillary site preparation & erosion control installations
  - Grubbing and shrub clearing
  - Monitoring well protection
  - Soil cover installation
  - Re-vegetation (late spring 2027)


•ARAR – Applicable or Relevant and Appropriate Requirements
•USAF – United States Air Force


"WIN AS ONE"

Site LF019 Remedial Action

- **Landfill Soil Cover Components:**
  - A subgrade layer on the existing ground surface prior to placement of up to 2 feet of cover material to achieve final grade
  - A fill layer of up to 18 inches of clean, borrow soil cover over the subgrade layer
  - Compaction of 90 percent (%) or greater and optimal moisture content +/-5%
  - A 6-inch (in.) topsoil layer to promote vegetation growth and erosion control

Site LF019 Remedial Action

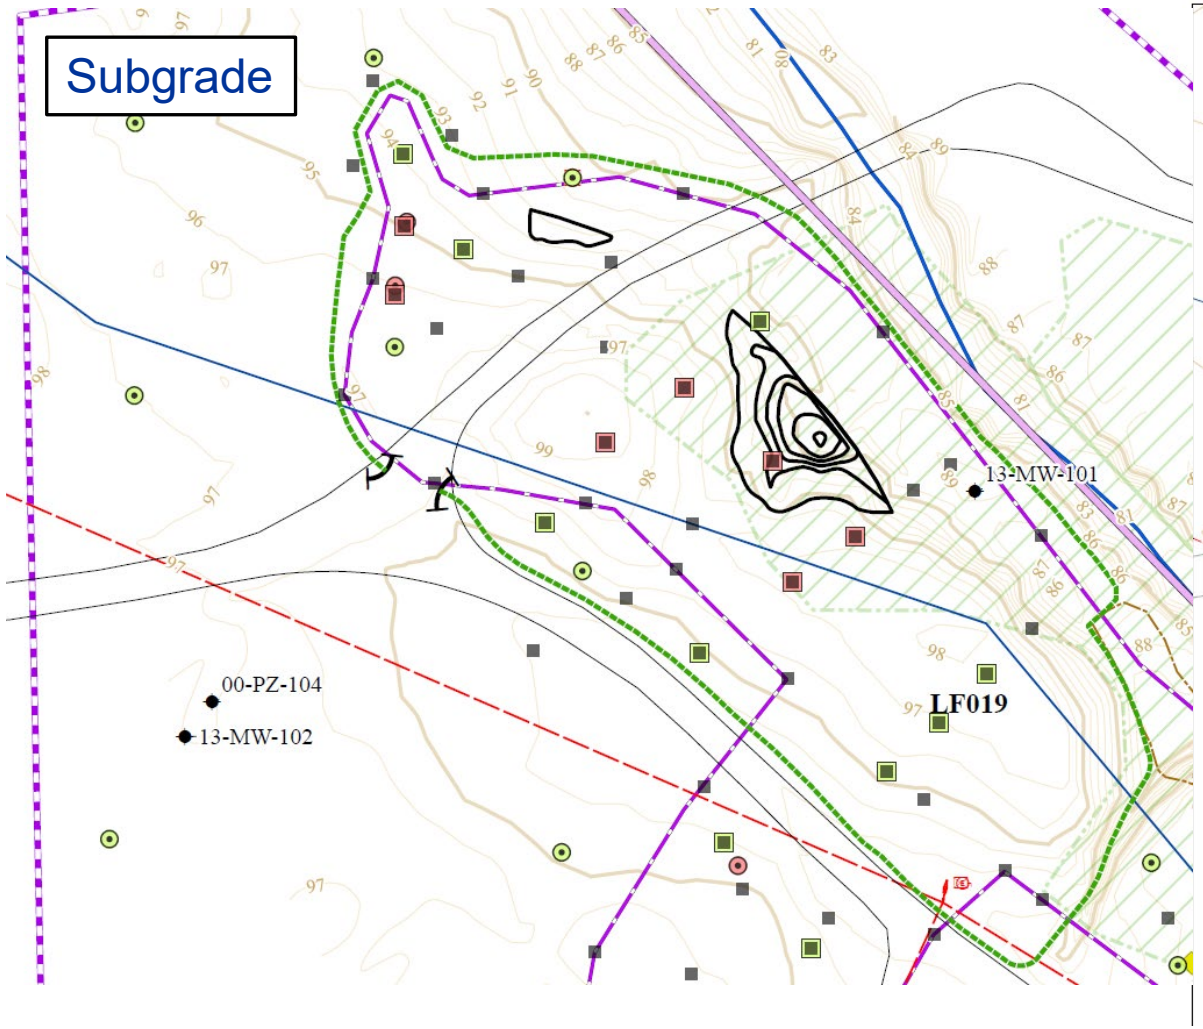

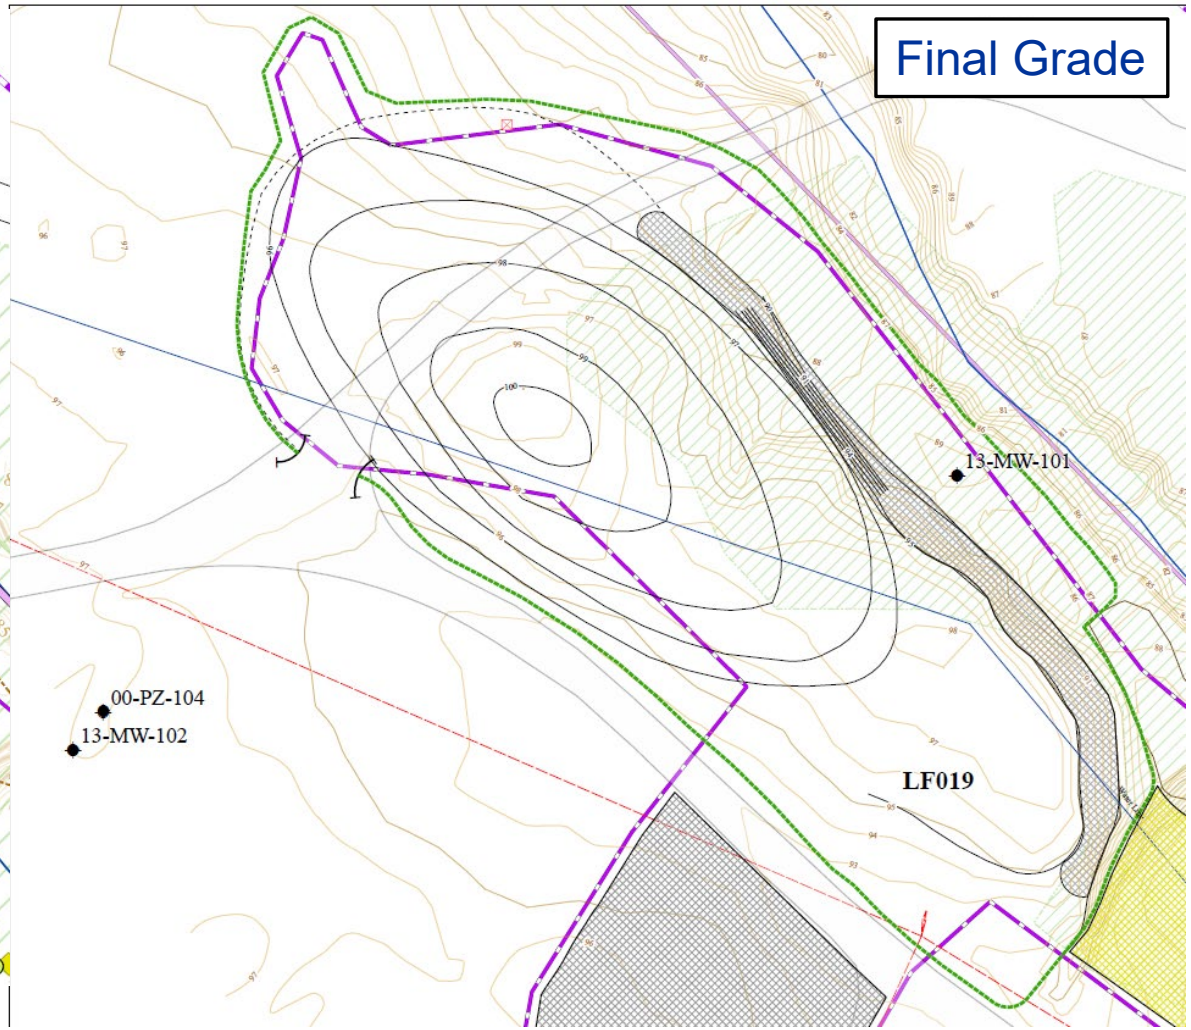

"WIN AS ONE"

Site LF019 Remedial Action

- Post-construction activities
  - Final surveying
  - Reinstallation of the road to ‘Back 40’
  - Verify soil stabilization and vegetation establishment (Spring/Summer 2027)
  - Conduct four quarters of groundwater and surface water sampling
  - Remedial Action Completion Report





Joint Base McGuire-Dix-Lakehurst
Dix Site TU972 (North Dogwood Lake)

Mr. Tom Crone

Project Manager, Arcadis Inc.


Site TU972 North Dogwood Lake

- TU972 is a former underground storage tank (UST) site regulated by the New Jersey Department of Environmental Protection (NJDEP)
- Added to the Optimized Remediation Contract in 2026 after a UST was found in 2023 during a water line installation. UST was removed in 2023 and initial soil sampling was completed

TU972 North Dogwood Lake



TU972 Site Location

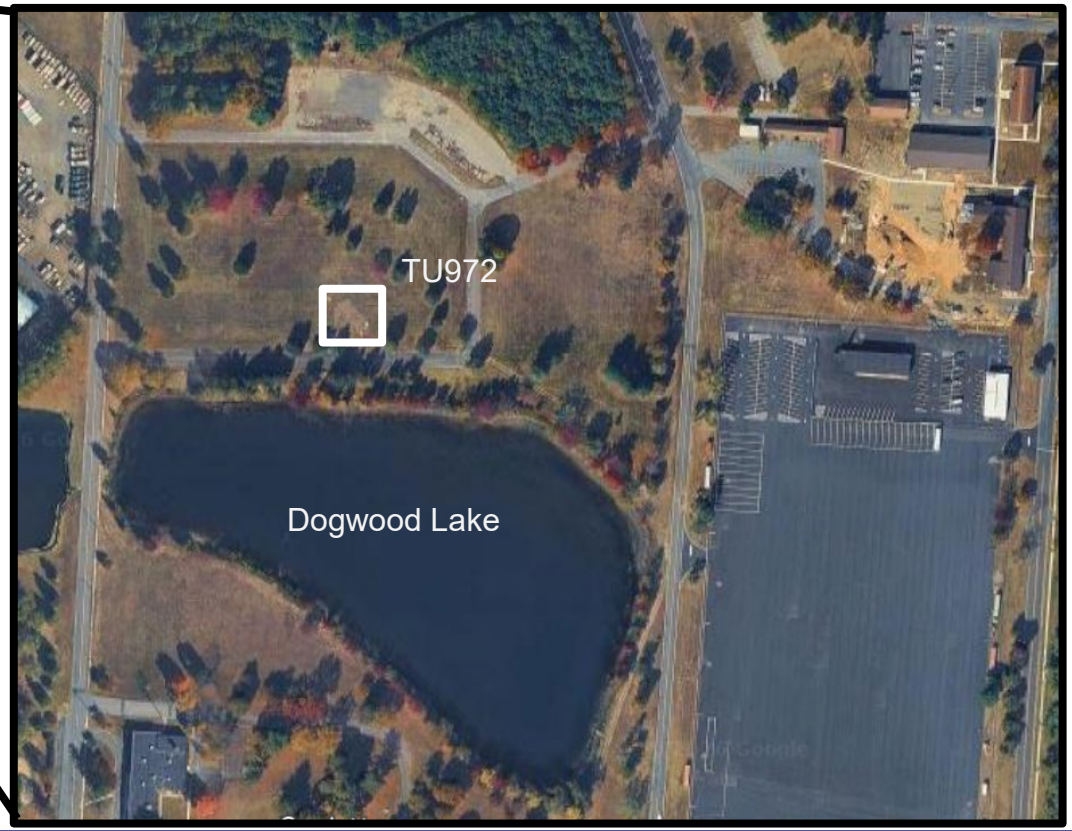



Underground storage tank removal in 2023

"WIN AS ONE"

Site TU972 North Dogwood Lake

- **FPM Team to complete a Preliminary Assessment/Site Inspection (PA/SI) within three years**
- **FPM Team will:**
  - **Prepare a PA/SI Workplan that complies with the applicable State (NJDEP) response laws (i.e., N.J.A.C. 7:26E – Technical Requirements for Site Remediation)**
  - **Field program will include soil, groundwater, sediment and surface water sampling downgradient of the former UST location and along the nearest edge of Dogwood Lake.**

•NJDEP – New Jersey Department of Environmental Protection





Optimized Remediation Contract (ORC)
Bridge Modification


Mr. Niels van Hoesel

Project Manager, FPM Remediations Inc.

ORC Introduction

- **Optimized Remediation Contract (ORC)**
  - Awarded September 2024
  - 10-year Firm Fixed Price (FFP) contract.
    - Years 2 completed. Year 3 ongoing
  - 75 sites
    - McGuire: 51 Sites (FPM/Arcadis)
    - Dix: 11 Sites (Arcadis)
    - Lakehurst: 13 Sites (EA/FPM)
- **Prime Contractor: FPM Remediations Inc.**
- **Teaming Partners: Arcadis & EA Engineering**

JB MDL Oversight Figure

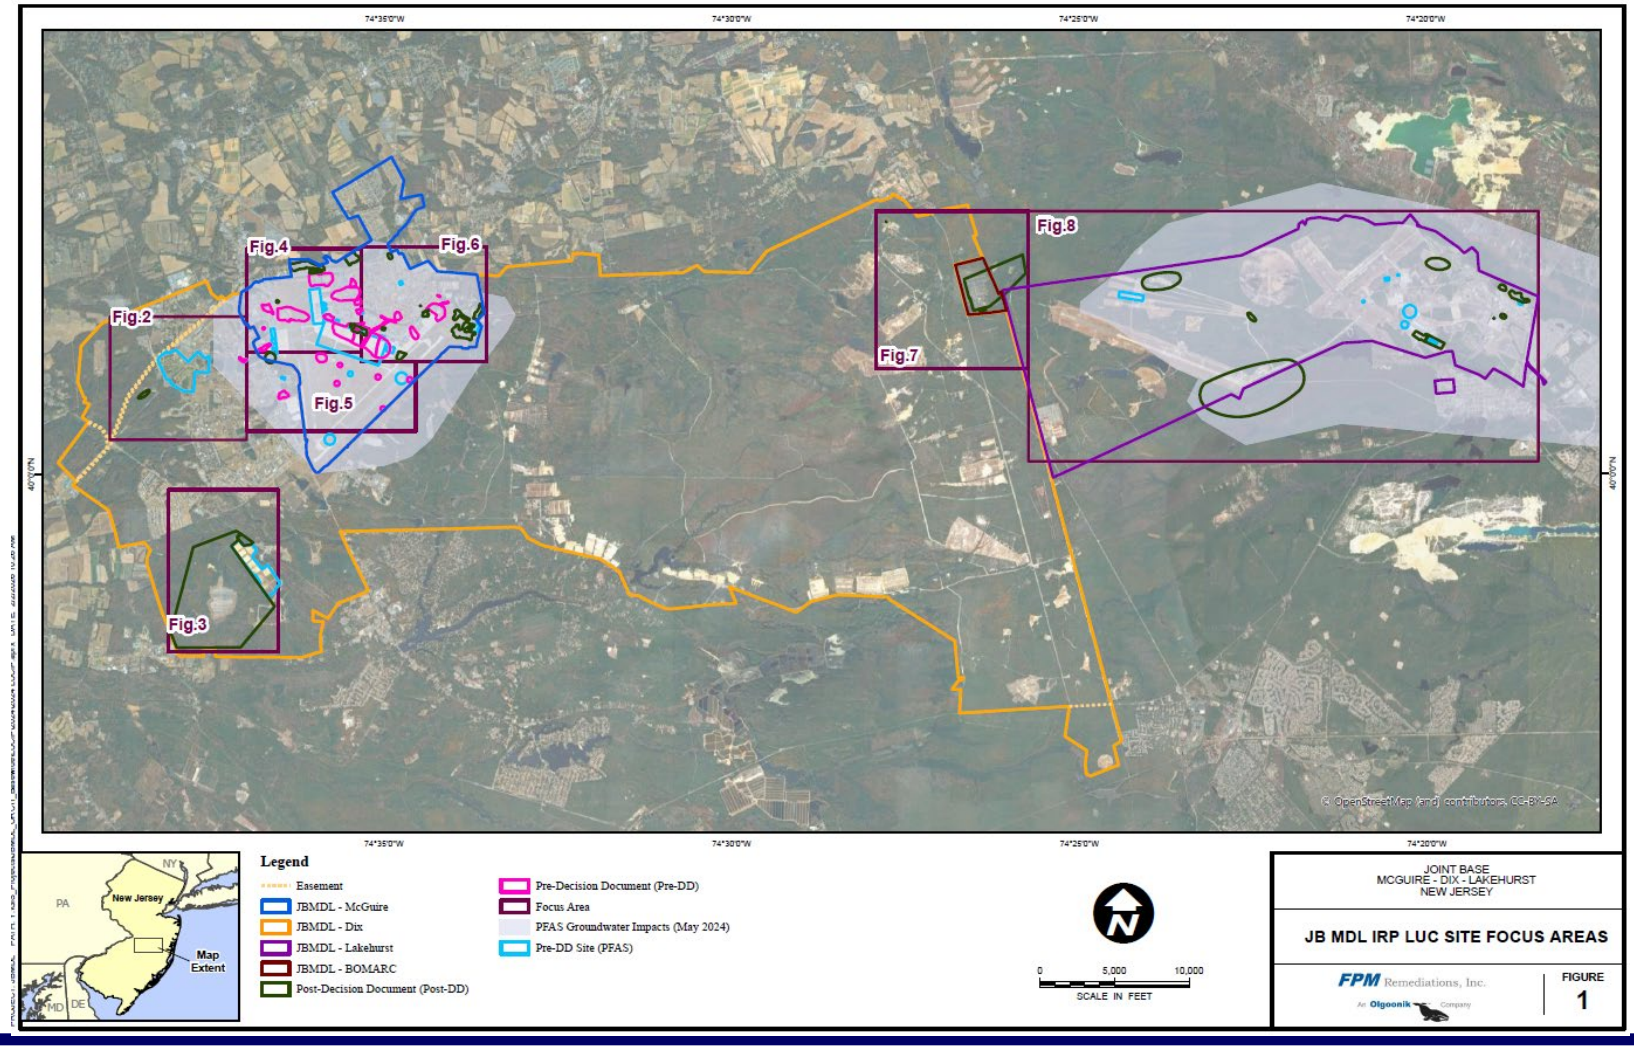

"WIN AS ONE"

Bridge Modification

- **Bridge Modification (awarded 9/30/2026)**
  - Modification to ‘bridge’ between the work not finalized during the last (pre-2024) PBR and the current (post-2024) ORC
  - Adds over 100+ additional tasks/milestones
  - Adds one new Dix site TU0972 (discussed as prior topic)
  - Includes escalation of postponed tasks initially awarded under the ORC
  - Most significant impacts to McGuire pre-Record of Decision sites at Operable Units-2, 5, 6, 7, and 8 (28 sites)
    - Prepare Migration to Groundwater (MGW) technical memoranda
    - Prepare updated Feasibility Studies (FSs)
    - Prepare updated Proposed Plans (PPs)
    - Schedules for initial tasks awarded under the ORC will shift to the right 2+ years
  - Work starts immediately and will continue through Fiscal Year 2027

•NJDEP – New Jersey Department of Environmental Protection
•ORC – Optimized Remediation Contract
•OU – Operable Unit
•PBR – Performance Based Remediation

“WIN AS ONE”





Per- and Polyfluoroalkyl Substances (PFAS) Anthropogenic Background Investigations

Mr. Mike Figura

Remediation Program Manager, AFCEC/CZOE

Anthropogenic PFAS Background Study

- Eleven Air Force Installations including JB MDL
  - USACE Mobile District
  - Period of Performance: Sept 2026 – Sept 2029
- Scope / Goals / Objectives:
  - Establish baseline anthropogenic PFAS levels associated with surface soil, shallow subsurface soil, overburden groundwater, surface water, and sediment
  - Groundwater : 15 wells – 2 rounds
    - Samples: New wells 2 each @ 55', @ 40', @ 30'
  - Soil: 15 borings – 5' below ground surface – 3 samples/boring
  - Surface Water/Sediment: 15 collocated samples – 2 rounds
  - Results will be used for assessing risk and remediation requirements

JB MDL – Joint Bae McGuire-Dix-Lakehurst
PFAS - per- and polyfluoroalkyl substances
USACE – United States Army Corps of Engineers

"WIN AS ONE"

Anthropogenic PFAS Background Study

- **Next Steps:**
  - **Initial Data Mining**
  - **Site Reconnaissance**
  - **UFP-QAPP/Work Plan**
    - **Scoping Meetings: Air Force; Regulators; Comment Resolution with Regulators**
  - **Field Execution**
  - **Statistical Analysis and Reporting**





East Region MCL Compliance and Drinking Water Mitigation Project

Mr. Mike Figura

Remediation Program Manager, AFCEC/CZRE

MCL – Maximum Contaminant Level

MCL Compliance and Drinking Water Mitigation

- Eleven Air Force Installations including JB MDL
  - Air Force Materiel Command 772 Enterprise Sourcing Squadron
  - Period of Performance: Aug 2026 – Aug 2027 (Base Year)
- Scope / Objectives:
  - Provide PFAS Drinking Water Sampling and Mitigation including sampling, treatment system installation, operation and maintenance, monitoring, and related program management activities
  - Planning documents (e.g. WP, UFP-QAPP, etc.) preparation and implementation
  - Drinking water sampling and monitoring
  - Point of Use Treatment System (POUTS) installation and startup
  - Operation & Maintenance (O&M) and performance monitoring
  - Cost Benefit and Technical Analysis

JB MDL – Joint Bae McGuire-Dix-Lakehurst
PFAS - per- and polyfluoroalkyl substances
UFP QAPP – Uniform Federal Policy Quality Assurance Project Plan
WP – Work Plan

"WIN AS ONE"

Point of Use Treatment System (POUTS)

- Treatment System Configuration
  - Under-sink point-of-use treatment system
  - Four-stage treatment process:
    - Sediment prefilter
    - Carbon block pretreatment filter
    - Water softening cartridge
    - PFAS-specific ion exchange cartridge
  - Post-installation (Influent and Effluent) sampling to verify system performance
  - Semi-annual monitoring and maintenance following installation

Schedule

- Draft WP / QAPP - September 2026
- Final WP / QAPP – October 2026
- Begin POUTS Installations – October 2026
- Complete POUTS Installations – End of 2026

POUTS – Point of Use Treatment System
QAPP – Quality Assurance Project Plan
WP – Work Plan

"WIN AS ONE"

Cost Benefit and Technical Analysis

- **Objective**
  - Evaluate long-term response actions for private drinking water wells with PFAS concentrations exceeding applicable MCLs
  - Complete all CBAs within six months of contract award (February 2027)
  - Provide recommendations to support selection of a long-term response action
- **Response Action Evaluation Hierarchy**
  1. Municipal Water Connection
  2. Point of Entry Treatment System (POETS)
  3. Point of Use Treatment System (POUTS)
  4. Long-Term Bottled Water Delivery

CBA – Cost Benefit Analysis
MCL – Maximum Contaminant Level
PFAS - per- and polyfluoroalkyl substances

"WIN AS ONE"





Future JB MDL Five-Year Review Schedule

Mr. Mike Figura

Remediation Program Manager, AFCEC/CZOE

JBMDL Five-Year Review (FYR) Schedule

JB MDL Area	Next Five-Year Review	Following Five-Year Review
McGuire	09/27/2027 (Statutory requirement for initiation of Operable Unti 1 Remedial Action)	01/14/2030 (Resetting to coincide with initial remedial action of first site at McGuire requiring a FYR)
Dix	05/09/2028 (5-years following last FYR)	08/15/2029 (Resetting to coincide with initial remedial action of first site at Dix requiring a FYR)
Lakehurst	09/27/2028 (Resetting to coincide with initial remedial action of first site at Lakehurst requiring a FYR)	09/27/2032 (5-years following last FYR)

QUESTIONS?
